

# Allatoona Update


Southeastern Federal Power Alliance

29 September 2015

Christopher S. Ludwig  
U.S. Army Corps of Engineers  
Mobile District



®  
US Army Corps of Engineers  
**BUILDING STRONG**®

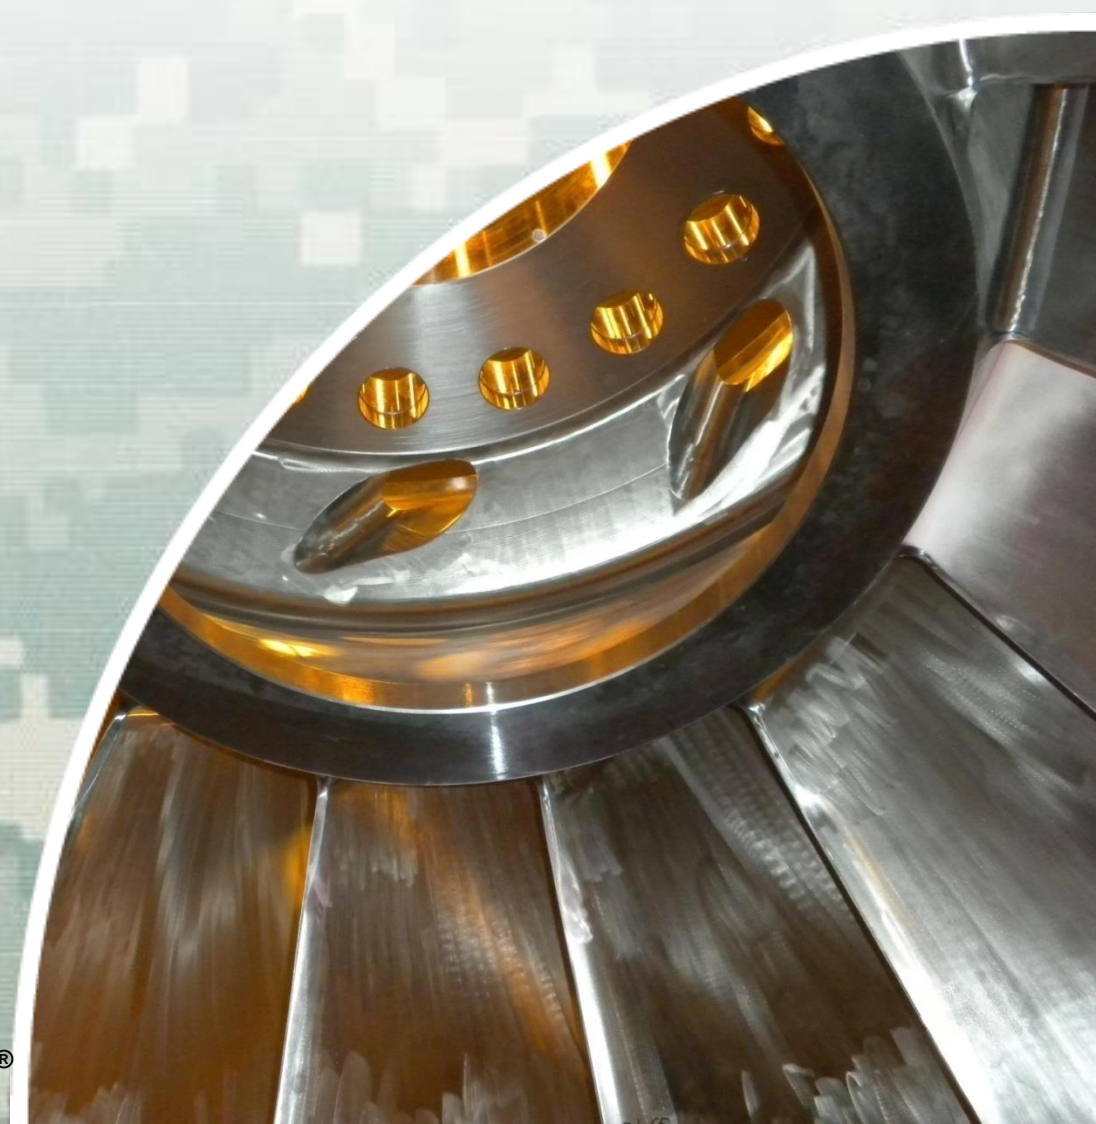

# Project Summary

- Environmental clean up complete
- Concrete damage determined to have no impact to structural integrity
- Koontz has returned to site and is executing remainder of work within the scope of their contract
- Customer funding sub-agreement #19 approved and provides \$10M to complete the balance of work necessary to restore power production capability.
- Switchyard and GSU transformer installation is complete
- First main unit return to service April 2017, second unit May 2017



# Tasks Currently Being Executed

- Concrete repairs – contractor currently on site performing repairs
- Renovation scopes for control room, spread room, and office areas complete and in contracting
- Crane repair scope complete in contracting
- Control system\SCADA design complete
- Governor specification development in progress
- Exciter specification development in progress
- Raw water piping removal\asbestos abatement in progress



# Future Tasks

- Generator disassembly\cleaning and testing – requires completion of crane repairs
- Powerhouse interior painting – requires completion of concrete repairs
- Raw water piping installation – requires completion of asbestos abatement and raw water piping removal
- Installation of SCADA\control system – requires completion of concrete repairs
- Replacement of digital microwave communication equipment – recently identified, requires replacement of equipment at Carters\Buford\Pinelog.



# Koontz

- Directed to complete original scope of work, any items not in original scope but now necessary to complete the scope due to the fire, and out of scope repairs necessary as a result of the fire and determined to be within their capabilities.
- Koontz has returned to work per Contracting Officer's direction however both they and their insurance companies are not admitting any liability or waiving an right to re-coup resulting additional expenses.
- Replacement switchgear equipment has begun to arrive at the plant
- Koontz has started removal of damaged equipment and preparing for installation of replacements.





# Current Status - Control Room



**BUILDING STRONG®**

# Current Status - Cable Tray Room



**BUILDING STRONG®**



# Current Status – Spread Room



**BUILDING STRONG®**



# Current Status – Switchgear Room



**BUILDING STRONG®**

# Questions?



**BUILDING STRONG®**
